ARBORICULTURAL METHOD STATEMENT

TREE WORKS

Only the tree works specified within this report may be undertaken, after the appropriate planning consents have been acquired and in order to implement the consent. In the event of any uncertainty regarding tree works, the retained arboricultural consultant will be consulted and where appropriate the Local Planning Authority.

All tree works will be undertaken, in accordance with the best-practice recommendations provided in BS 3998:2010. The statutory responsibilities as outlined in the Wildlife and Countryside Act 1981 (as amended) and the Habitat Regulations 2010 will also be complied with.

TREE PROTECTION FENCING

The tree protection fencing and (where appropriate) ground protection, will be installed as specified within this plan, prior to the commencement of any demolition and construction works. No plant or materials will be delivered to site prior to the construction of the tree protective fencing other than those required to install the tree protection fencing. On every third panel, a sign will be fixed that states "*Tree Protection Zone (TPZ). Keep out. Any incursion into this area must be agreed in advance with the retained arboricultural consultant and Local Planning Authority*." An example of this sign is provided within this plan.

The position of the tree protection fencing must not be amended and no individual panels will be uncoupled, without the agreement of the retained arboricultural consultant and/or Local Planning Authority.

SERVICES AND DRAINAGE

The installation of drainage runs, manholes, storage tanks, and utilities will be positioned outside the root protection areas of retained trees. If the installation of new services and drainage runs are required within the root protection areas (RPAs) of retained trees, all methods of working will follow the guidance within Table 3 of BS 5837 or the National Joint Utilities Group's (NJUG) Guidelines for the planning, installation and maintenance of utility apparatus in proximity to trees (volume 4, issue 2).

Excavation works within the RPAs of retained trees will be undertaken manually with the use of hand tools only (under the supervision of the retained arboricultural consultant), unless otherwise agreed in advance by the retained arboricultural consultant. It is recommended that an air lance - and if required a soil vacuum - is used, to excavate service trenches within RPAs. If soil conditions are not suitable for this method of excavation, alternative hand tools can be used once agreed in advance by the retained arboricultural consultant.

All roots greater than 25mm in diameter will be retained and will immediately be wrapped in hessian or another appropriate material, to prevent desiccation and temperature fluctuations. Roots will be pushed aside to allow for runs to be installed, where this is practical and without causing root damage.

No machinery will be permitted within the TPZ, at any time, unless agreed in advance with the retained arboricultural consultant.

NO-DIG CONSTRUCTION AREAS

Areas that will require no-dig methods of construction are shown within this plan. Working methods within these areas will comply with the details outlined in the main report and in advance of works being undertaken will be agreed with the retained arboricultural consultant.

ARBORICULTURAL CLERK OF WORKS

The monitoring of activities at the Site will occur, at the following points:

- To sign-off the tree protection measures;
- To sign-off the tree works;
- At other points as specified within this Report and the TPP.

It will be the responsibility of the main contractor (or other managing individual or organisation) to confirm the date and time of attendance, providing at least five working days of notice so that the project arboriculturist can confirm attendance.

GENERAL PROTECTION METHODS

No fires will be permitted, within 20m of the crown of any tree or other area of vegetation that includes hedgerows and groups of trees.

No changes in soil level will occur, within the TPZs and RPAs, without agreement in advance with the retained arboricultural consultant.

The TPZs will at all times remain free of liquids, materials, vehicles, plant, and personnel, without agreement in advance with the retained arboricultural consultant.

Any liquid materials spilled on site will immediately be cleared up. If liquids are spilled within 2m of any TPZ or RPA, the incident will immediately be reported to the retained arboricultural consultant, to determine the appropriate response.

All damage to trees and other vegetation will immediately be reported to the retained arboricultural consultant, to determine the appropriate response.

Figure 3 Examples of above-grounds stabilizing systems

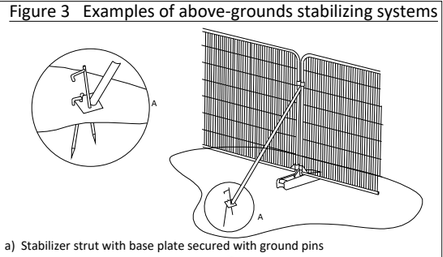

a) Stabilizer strut with base plate secured with ground pins



b) Stabilizer strut mounted on block tray

N

The original of this drawing was produced in colour -a monochrome copy should not be relied upon.

BS 5837:2012 TREE RETENTION CATEGORIES

Category A
Trees of high quality with an estimated remaining life expectancy of at least 40 years.

Category B
Trees of moderate quality with an estimated remaining life expectancy of at least 20 years.

Category C
Trees of low quality with an estimated remaining life expectancy of at least 10 years or young trees with a stem diameter below 150mm.

Category U
Those in such a condition that the tree cannot realistically be retained as living trees in the context of the current land use for longer that 10 years.

BS5837 Root Protection Areas
Precautionary areas within which tree roots and soil structure must be protected. All works within these areas will require special methods of work.

Position of protective fencing and tree protection zones during construction. Position may be amended for landscaping.

Location of ground mats during construction to allow working room and pedestrian access round the proposed building.

REV	DATE	DESCRIPTION	DRAWN
-	xx.xx.xx	-	xx

Base Drawing

-	-	-

Title
Tree Protection Plan

Client
HADSCAL

Project
HADSCAL Land, Hay-on-Wye, HR3 5DY.

Date	Drawn by	Checked by
October 2026	EC	-
Drawing No	**Rev**	**Scale**
3528-P-12	-	1:1000 A3

focus
ENVIRONMENTAL CONSULTANTS
